



P.21-15 Rail To River - Public Realm Project Highlight Report

Project Name:	Rail To River - Public Realm	Project Manager	Abigail Rawlings	Project Sponsor:	Duncan Hall	Report covers period of:	July 2025
Capital Code:	C9064	Client Dept:	Regeneration	Lead Designer:	-	Cost Consultant:	-
Project Code:	P-21.15	End User (if applicable):	n/a	Contractor on Site:	-		

Management Summary

	1.Overall Status	2.1 Risks	2.2. Issues	3.Financials	4.Timelines	5.Resources
This Report	G	G	A	G	A	G
Last Report	G	G	A	G	A	G

Project Definition

Project Stage: RIBA stage 6 handover.

RIBA stage 5 – manufacturing and construction (arch only)

Objectives: Improve public realm in the town centre to improve the pedestrian experience, removing clutter, creating consistent public realm experience

Scope: Rail to River route works include providing interventions such as pop-up facilities, art trail, fingerpost wayfinding, lighting, seating and planting.

1. Overall Status (high-level summary)

Overall Status currently GREEN.

- Businesses have been operating from the Pop Ups since March.
- Artwork, seating and wayfinding digital sign installed.
- 14 trees and bespoke planters installed on Purfleet Street, New Conduit Street and Broad Street.
- Handover to Business as usual for Pop Ups and digital sign.
- The Purfleet Street Arch is now the only outstanding item.

1.1 Decisions required by the Neighbourhood Board

- None required at this July board

1.2 Achievements during this period

- Solution found for Pop Up Wi-Fi issue that was causing occupant payment issues.
- Meeting with Operational team to discuss issues to occupation caused by scaffold on street.

2. Risks and Issues

2.1 Key Risks [all red and increasing amber] A risk is something that may happen

Risk ID (2/22)	Risk Title	Description	RAG Status	Risk Category	Mitigation	Dated Comments
	No response or suitable responses to RfQ for Purfleet Street Arch	Failure to get suitable responses to RfQ for the Purfleet Street arch would result in this element of the project not taking place.	A	Low	Previous RfQ received sufficient responses suggesting artists are willing to quote for the work. Requirement for the arch to be hand forged is removed,	30/07/2025




					widening the options for craftspeople to quote.	
	Planning application for Cashino building.	New planning application from owner of Cashino building proposes a new floor to the building. This may have an effect on the arch install.	A	Low	Contact to be made with owner to ask if the arch install will be taken into account in plans.	30/07/2025

2.2 Key Issues [all red and increasing amber] – An issue is something that has happened

Issue ID (1/6)	Issue Title	Description	RAG Status	Issue Type	Resolution Plan	Dated Comments
	Licence with Boots for Purfleet Street Arch	Boot's solicitor was unable to sign the licence due to scaffolding works taking place on Boots roof. Works now complete but Licence still not being completed by Boots.	A	Delay to programme	This is being chased by BCKLWN legal team. This will be picked up again in light of the building fire and the effect it will have on the licence/install onto the building.	30/07/2025

3.1 Project Financials

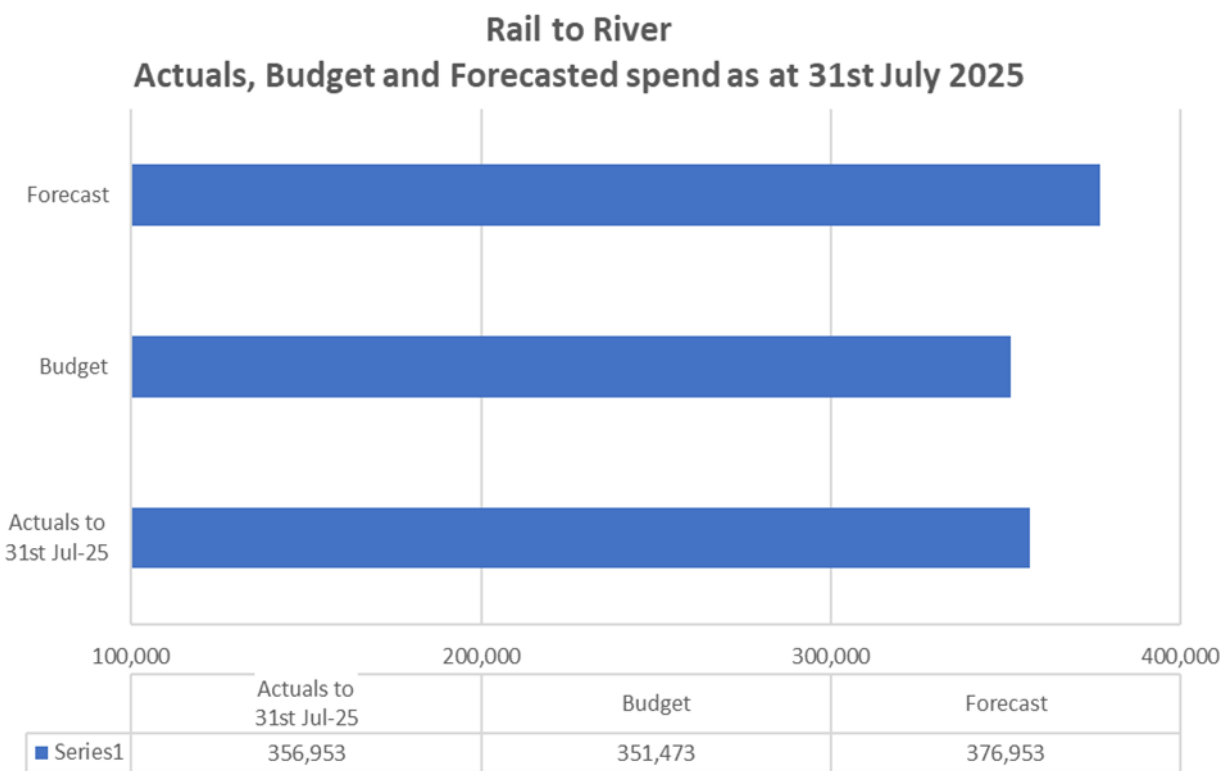

3.2 Financial Commentary


- Financials are maintained at GREEN.
- As of 31st July, overall project costs are £0.36m against a budget of £0.35, forecasted costs are £0.38m.

3.3 Project Contingency and Change Control

Change Ref	Description	Cost Impact	Programme Impact	Other Impact	RAG Status	Approval given by	Date of change



4. Timelines – High Level Milestones

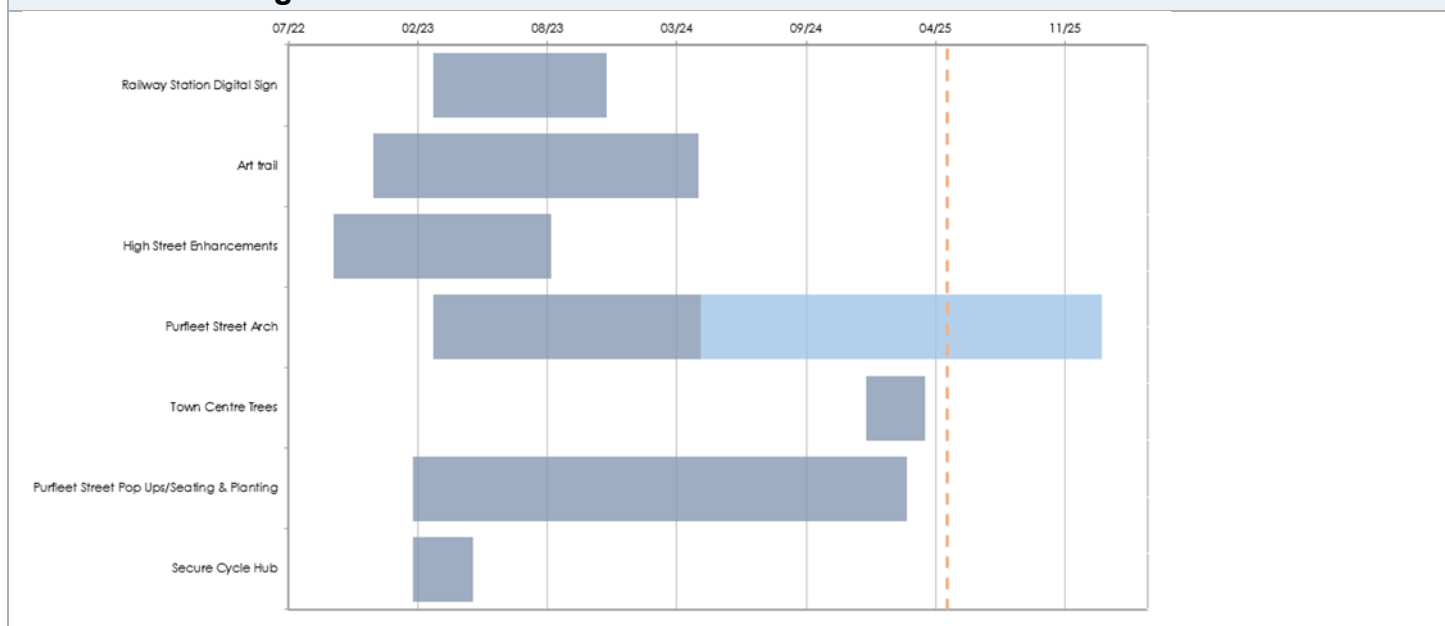

4.1 Timelines Commentary

- Timelines currently RAG rated AMBER. The proposed Arch at Purfleet Street is the only outstanding item. The proposed site to attach the arch to is covered in scaffold following a fire and would not currently be suitable to attach the arch.
- All other items have been installed/completed. The delay with the arch does not affect any funding timescales.

5. Resources Commentary

Resources currently RAG rated GREEN.

6. Communications and Engagement

Publicity of the Pop-Up businesses continues via social media channels and in partnership with King's Lynn BID.
Press enquiry from The Lynn News about the occupation of the units, site meeting arranged with reporter for early August

7. Outputs and Outcomes

7.1 Outputs

Description	Target	Notes
Increased footfall in the town centre	5%	
Footfall counts	1	
Number of transport nodes with new multimodal connection points (cycle storage)	1350m2	
Amount of public realm improved m ²	5	
No of businesses supported	5+	4 pop up units supporting a number of businesses throughout the project.
No of trees planted	5	14 trees planted
Number of Finger post installations	30	
Number of artwork installations	3	Including archway, 2 currently installed.

7.2 Outcomes

Description	Notes
Increased footfall in the town centre	
Improve the accessibility and attractiveness of key routes	



Improve the perception of the place by residents, visitors and businesses	
---	--

8. Other Matters

Item	Comment
General stage progress	Design and installation: Railway Station Benches and planting – complete Digital Sign – complete Artwork x 2 – complete. Purfleet Street Arch – delayed. All planning and NCC licenses in place. Purfleet Street Pop Ups and street furniture installed. Utilities – water and electricity connections have been installed, issue with drainage resolved. Installed Cycle hub – complete. Purfleet Street planters- complete.
Procurement progress	Individual project elements; with in house co-ordination. Remaining orders to place – new Purfleet Street arch order.
Proposed form of contract (e.g., JCT, NEC, Traditional, D&B)	A variety of contracts will be used. In some cases, they are suppliers T&C's, in other they are on standard council terms. As we do not have a one stop shop approach, each element is procured independently, and the council is acting as the contractor.
Proposed route to market (e.g., IOTT, Framework i.e. DPS, HPCS, LCP)	Single source supply for digital sign, containers, steelwork cladding, and archway. Other - Invitations to Quote, Locally Advertised, and approved local contractors as per standing orders.
Legal progress	License to fix arch to Boots and Cashino buildings with legal. Flyover licenses with NCC for archway. Pitch licenses with NCC and Street trading licences for pop ups. Application for tables and seating required by NCC.- complete. Application for planters on highway required by NCC complete.
Local schemes / dependencies	Licensing process for digital signage with Network Rail has conditional approval. Final information of as fitted drawing and fire stopping report needed from Hollywell to complete sign off- being sought from Hollywell.

9. Approved Documents

	OBC [RIBA 0 Approval]	Client Brief [RIBA 1 Initiation]	Resource Brief	PID [RIBA 1 Gateway]	PID Update [RIBA 2 Gateway]	PID Update [RIBA 3 Gateway]	PID Update [RIBA 4 Design]	Final PID [pre-post tender]
Status:	✓	✓	✓	✓	✓	✓		
Date Approved:	Jan 2022					Feb 2023		
Approved by:	KLTB					KLTB		

Latest approved document: PID November 2023

Spend – Budget variance (Inc. Contingency)	Milestone Delivery RAG Status	Risk & Issue RAG status
R More than 10% over or under budget	R 13 weeks or more behind the critical path	R Need immediate attention
A Between 5% & 10% over or under budget	A 4 to 12 weeks behind the critical path	A Needs attention before next project review
G Within 5% of budget or less than £10k	G 4 to 12 weeks less behind the critical path	G Can be managed
